

PLATFORM TEAM • WEEK OF 8 JUNE 2026

# Lumen Platform

The checkout migration is on track for 1 July — one risk needs a decision today.



# Bottom line: we ship checkout on Lumen 1 July, on plan, with one open call.

---

The migration of checkout to the Lumen platform is 78% complete and tracking to the 1 July cutover. Eleven of fourteen services are live in production. The only thing standing between us and the date is a load-testing decision I need from this room today.



# Why this matters now: the legacy checkout stack goes end-of-support 31 July.

---

The vendor pulls security patches for the legacy stack at the end of July.

Migrating to Lumen before then keeps us supported and cuts our per-transaction cost by a third. Slipping past 1 July compresses the buffer between cutover and end-of-support to nothing.

- A clean two-week buffer is the difference between a calm launch and a forced one.
- Every week of delay is roughly \$40K in avoidable legacy hosting spend.



# Eleven of fourteen live; latency and errors inside target.

78%

Services migrated

11 OF 14 • TARGET 100% BY 1 JUL ON PLAN



142 ms

p99 checkout latency

TARGET 180 MS ON PLAN

0.02%

Checkout error rate

TARGET 0.1% ON PLAN



SHADOW TRAFFIC • LAST 7 DAYS

# What the shadow deployment is telling us before we cut over.

*Lumen running in parallel with legacy, mirroring 100% of live checkout traffic.*

4.1M

SHADOW TXNS  
PROCESSED

99.98%

PARITY WITH  
LEGACY

38

MISMATCHES  
INVESTIGATED


0

UNRESOLVED  
DISCREPANCIES



PROGRESS • Q2 2026

# How the migration has unfolded since April.

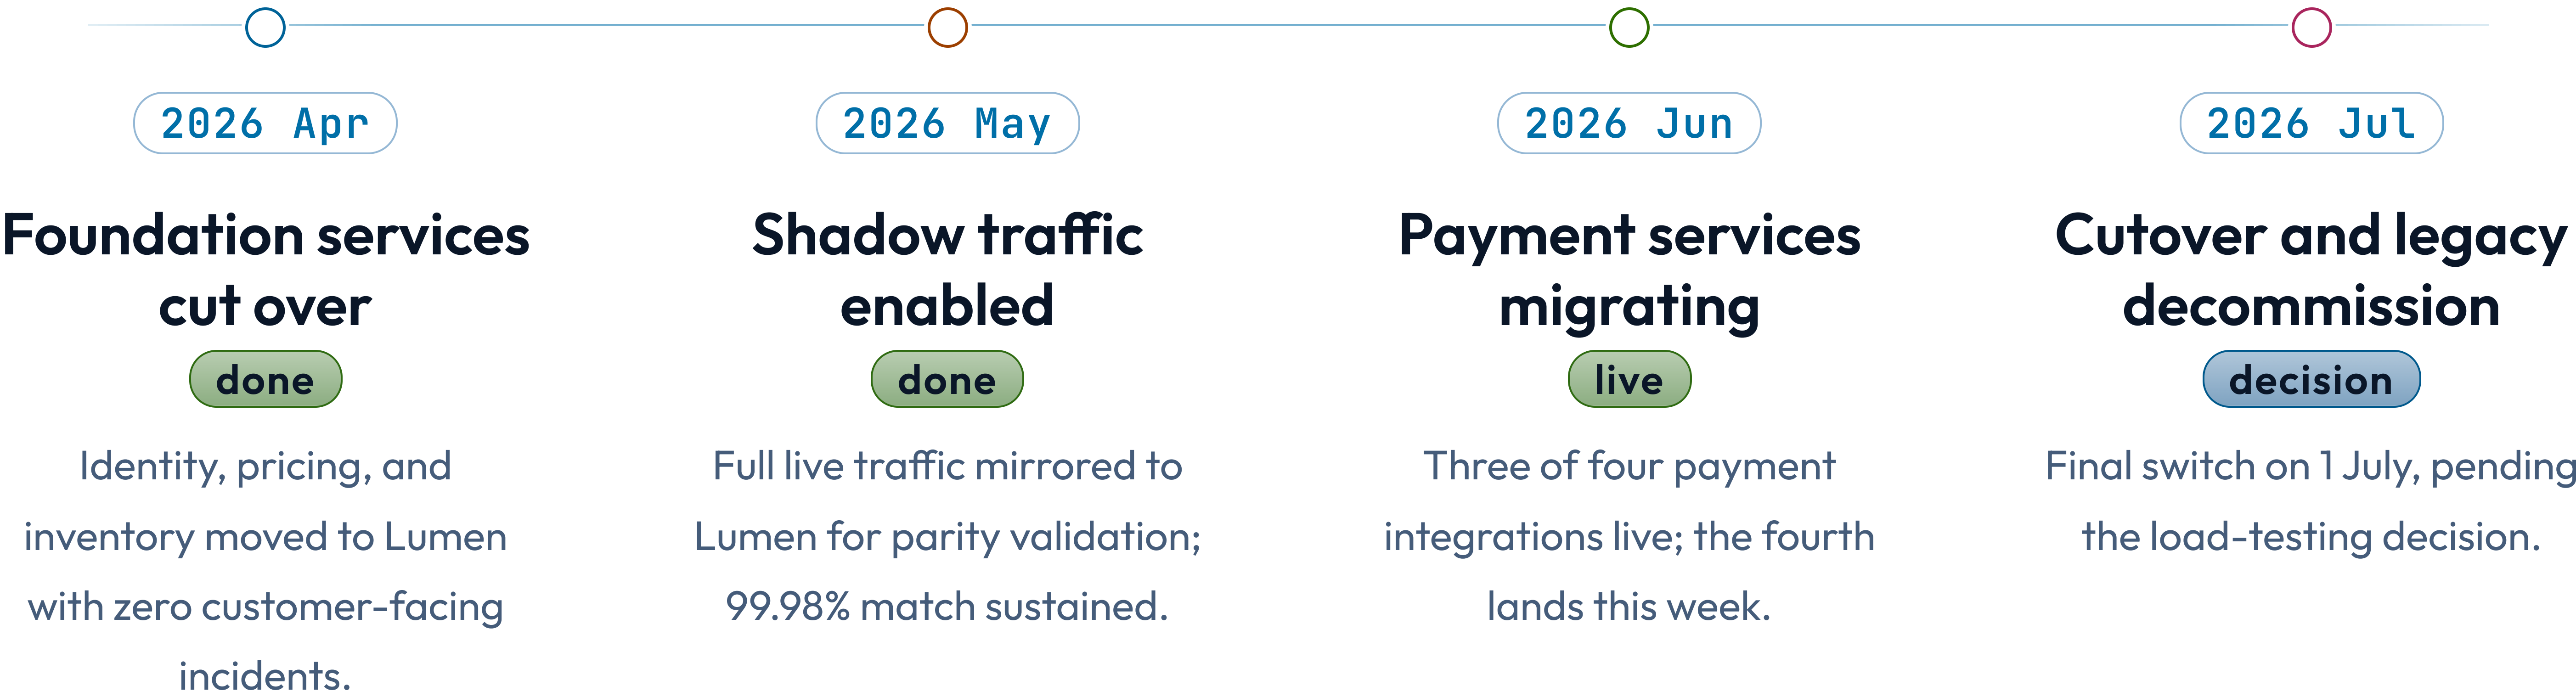



# What remains, by workstream, before we flip the switch.

| WORKSTREAM   | THIS WEEK         | NEXT WEEK       | CUTOVER         |
|--------------|-------------------|-----------------|-----------------|
|              | WK OF 8 JUN       | WK OF 15 JUN    | WK OF 29 JUN    |
| Services     | ✓ Payments 3 of 4 | – Final service | ○ Decommission  |
| Load testing | – Peak-load run   | ○ Sign-off      | ○ Standby       |
| Runbook      | ✓ Draft complete  | – Dry run       | ○ On-call brief |

✓ Shipped      – In flight      ○ Planned



# Where our open risks sit by likelihood and impact.

**Low likelihood • Low impact.**

Documentation lag on internal APIs

**Low likelihood • High impact.**

Payment-gateway timeout under peak load

**High likelihood • Low impact.**

Minor dashboard parity gaps post-cutover

**High likelihood • High impact.**

Unrehearsed peak load on cutover day



# Cutover readiness as of today.

|   |                                     |                   |
|---|-------------------------------------|-------------------|
| ✓ | Shadow parity sustained above 99.9% | 7 days            |
| ✓ | Runbook drafted and reviewed        | Eng + SRE         |
| — | Peak-load run                       | awaiting decision |
| — | Rollback procedure                  | dry-run pending   |
| ○ | Final payment service live          | this week         |
| ○ | Executive go / no-go                | 25 Jun            |



# Decision today: run a full peak-load rehearsal before cutover.

## RUN THE PEAK-LOAD REHEARSAL

One day of effort buys certainty that checkout holds at Black-Friday volume.

## CUT OVER ON SYNTHETIC TESTS ONLY

Saves a day but leaves the highest-impact risk unrehearsed on launch day.



PRIYA VENKAT • PLATFORM-TEAM@LUMEN.EXAMPLE

On track for 1 July — pending  
your call on load testing.
