

MONTHLY STATUS • 10 JUNE 2026

Project Atlas

The mobile rebuild is on schedule and on budget — one dependency is now our top risk.

Atlas is green on schedule and budget; the auth vendor is our one amber risk.


The native mobile rebuild is 64% complete, tracking to the September beta and within budget. Engineering velocity is steady. The single item that could move the date is our dependency on the auth vendor's new SDK, which has slipped twice.

Why the rebuild: the old hybrid app caps our growth.

The current hybrid app crashes at three times the industry rate and can't use the device features our roadmap needs. Atlas rebuilds it natively so we stop losing users at launch and unblock the feature pipeline for the next two years.

- Crash rate today is 1.8% of sessions, against a 0.5% industry benchmark.
- Two roadmap features are blocked entirely by the old architecture.

On schedule and on budget; one workstream amber on a vendor dependency.

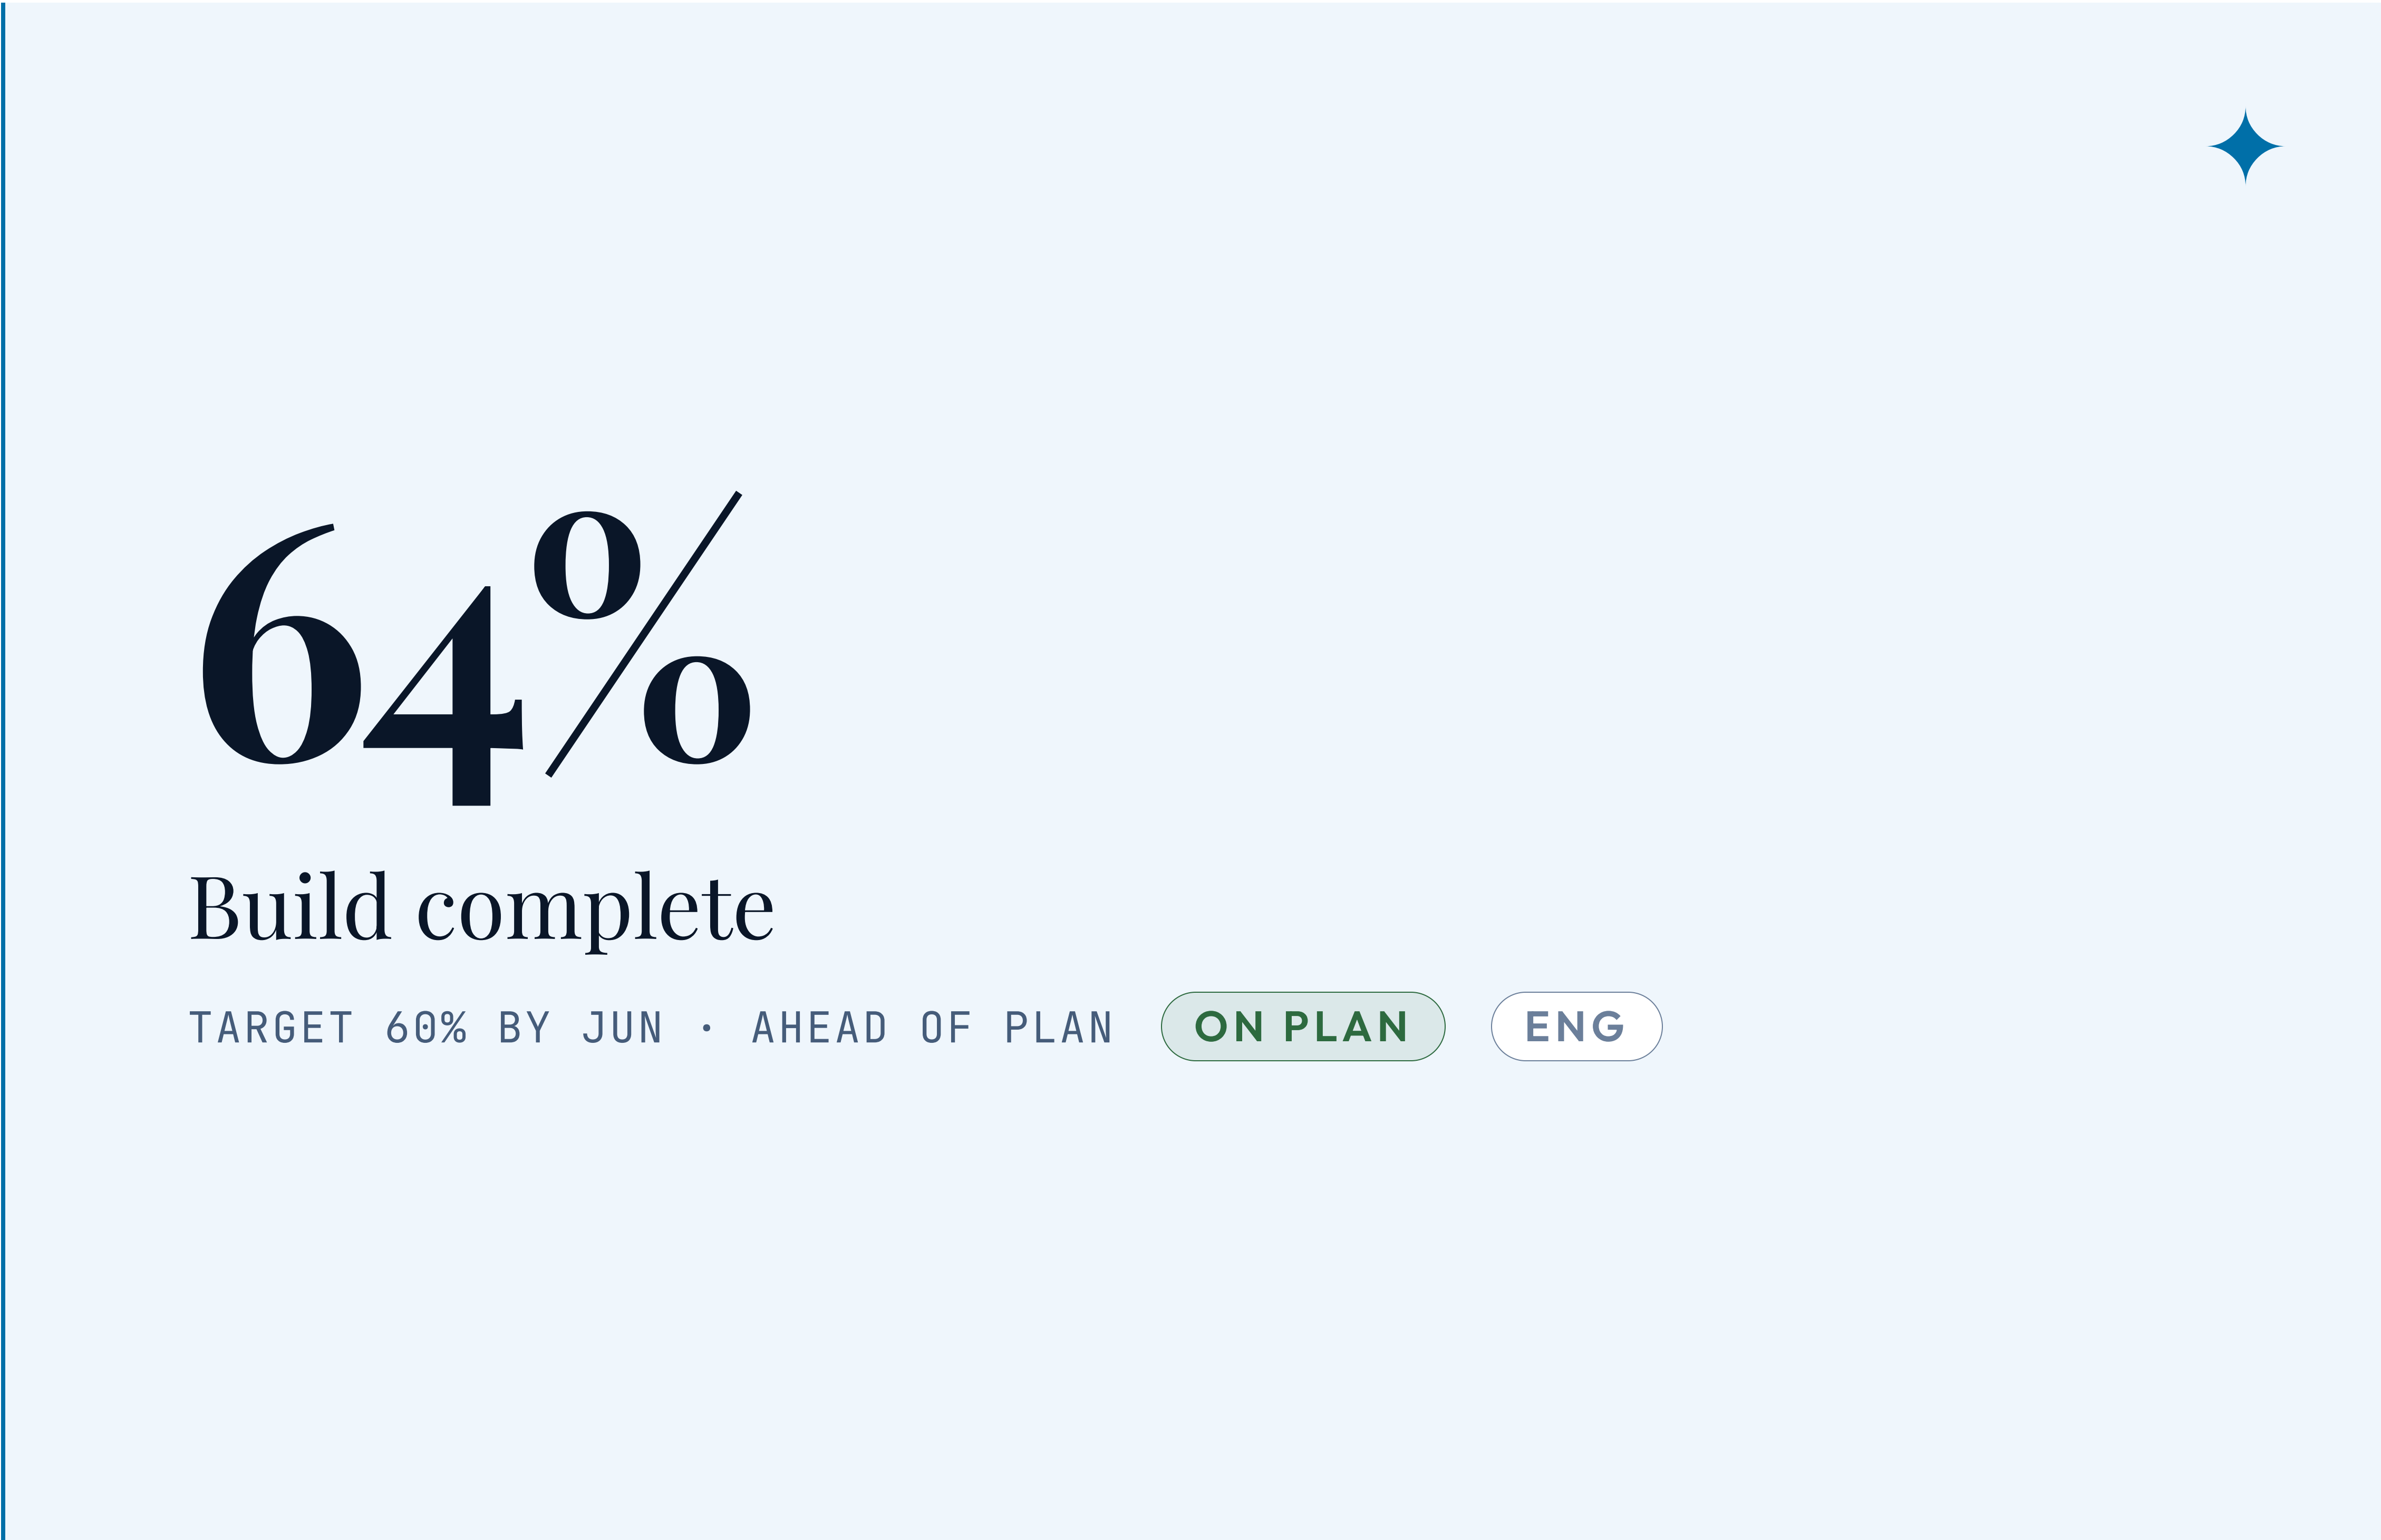

\$1.4M

Budget consumed

OF \$2.2M • 63% SPENT, 64% DONE

ON PLAN

FINANCE

1

Workstreams at risk

AUTH SDK DEPENDENCY

AT RISK

ENG

QUALITY • INTERNAL BUILDS

What the nightly builds tell us about quality so far.

MEASURED ON THE INTERNAL DOGFOOD BUILD ACROSS 320 TESTERS, LAST 30 DAYS.

0.4%

CRASH RATE

1.9s

COLD-START TIME

96%

AUTOMATED TEST COVERAGE

−67%

CRASHES VS HYBRID

Where each workstream stands against the September beta.

WORKSTREAM

NOW

NEXT

BETA

	JUN	JUL	SEP
Core UI	✓ Navigation shell	– Feature screens	○ Polish pass
Auth	– SDK integration	○ Biometric login	○ Hardening
Data sync	✓ Offline cache	– Conflict handling	○ Load test
Release	✓ CI pipeline	○ Beta channel	○ Store submission

✓

 Shipped


–

 In flight

○

 Planned

How the project has tracked since we started.

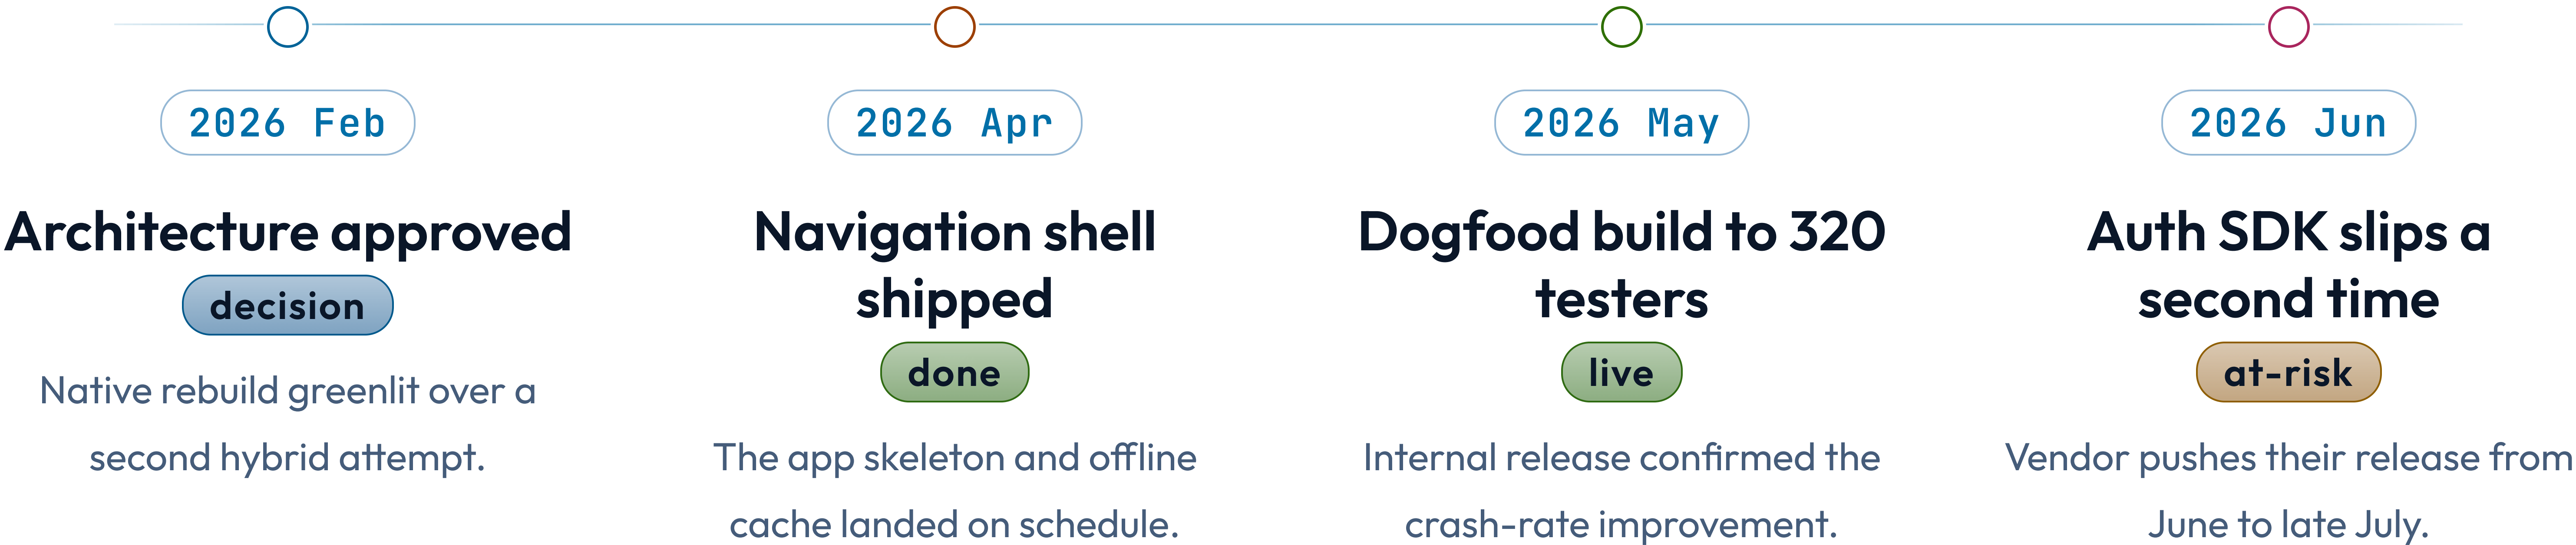

Our open risks, placed by likelihood and impact.

Low likelihood • Low impact.

App-store review delay

Low likelihood • High impact.

Data-sync conflict bug at scale

High likelihood • Low impact.

Minor UI polish slipping past beta

High likelihood • High impact.

Auth SDK slips again and blocks beta

Beta-readiness checklist.

✓	Navigation and core screens	complete
✓	Offline cache and sync	complete
—	Auth integration	blocked on vendor
—	Performance budget	1.9s, target 1.5s
○	Beta channel and tester onboarding	Jul
○	Store metadata and screenshots	Aug

To protect the date, we are building an auth fallback in parallel.

BUILD A FALLBACK TO THE CURRENT SDK

Two engineers for one sprint keeps beta on track if the vendor slips again.

WAIT FOR THE VENDOR'S NEW SDK

Cleaner long-term, but bets the September date on a date that has already moved twice.

LENA PARK · ATLAS@EXAMPLE.COM

Green on schedule and
budget — watching the
auth dependency
closely.
