

PLATFORM TEAM • WEEK OF 8 JUNE 2026

Lumen Platform

The checkout migration is on track for 1 July — one risk needs a decision today.

Bottom line: we ship checkout on Lumen 1 July, on plan, with one open call.

The migration of checkout to the Lumen platform is 78% complete and tracking to the 1 July cutover. Eleven of fourteen services are live in production. The only thing standing between us and the date is a load-testing decision I need from this room today.

Why this matters now: the legacy checkout stack goes end-of-support 31 July.

The vendor pulls security patches for the legacy stack at the end of July.

Migrating to Lumen before then keeps us supported and cuts our per-transaction cost by a third. Slipping past 1 July compresses the buffer between cutover and end-of-support to nothing.

- A clean two-week buffer is the difference between a calm launch and a forced one.
- Every week of delay is roughly \$40K in avoidable legacy hosting spend.

Eleven of fourteen services live; latency and error budget both inside target.

78%

Services migrated

TARGET 100% BY 1 JUL • 11 OF 14

ON PLAN

ENG



142 ms

p99 checkout latency

TARGET 180 MS • -21% HEADROOM

ON PLAN

SRE

0.02%

Checkout error rate

TARGET 0.1% • WELL INSIDE BUDGET

ON PLAN

SRE

SHADOW TRAFFIC • LAST 7 DAYS

What the shadow deployment is telling us before we cut over.

LUMEN RUNNING IN PARALLEL WITH LEGACY, MIRRORING 100% OF LIVE CHECKOUT TRAFFIC.

4.1M

SHADOW TXNS PROCESSED

99.98%

PARITY WITH LEGACY


38

MISMATCHES INVESTIGATED

0

UNRESOLVED DISCREPANCIES

How the migration has unfolded since April.

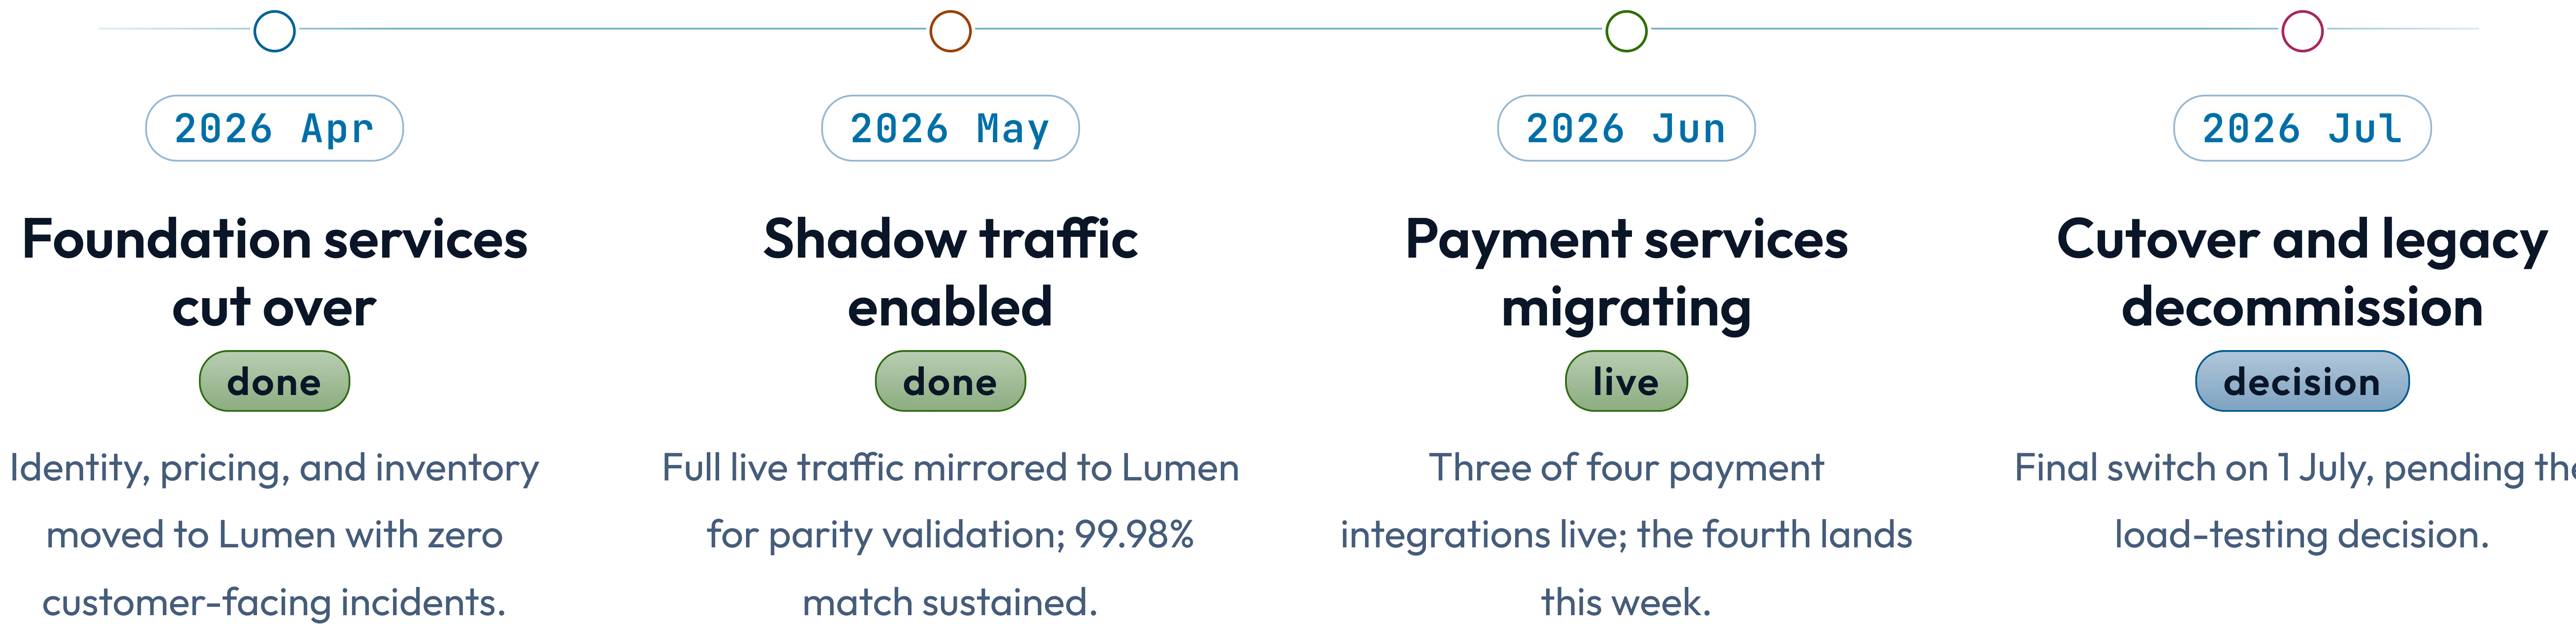

What remains, by workstream, before we flip the switch.

WORKSTREAM	THIS WEEK	NEXT WEEK	CUTOVER
	WK OF 8 JUN	WK OF 15 JUN	WK OF 29 JUN
Services	✔ Payments 3 of 4	✖ Final payment service	○ Decommission legacy
Load testing	✖ Peak-load rehearsal	○ Sign-off	○ Standby
Runbook	✔ Draft complete	✖ Dry-run rehearsal	○ On-call brief

✔ Shipped ✖ In flight ○ Planned

Where our open risks sit by likelihood and impact.

Low likelihood • Low impact.

Documentation lag on internal APIs

Low likelihood • High impact.

Payment-gateway timeout under peak load

High likelihood • Low impact.

Minor dashboard parity gaps post-cutover

High likelihood • High impact.

Unrehearsed peak load on cutover day

Cutover readiness as of today.

✓	Shadow parity sustained above 99.9%	7 days
✓	Runbook drafted and reviewed	Eng + SRE
—	Peak-load rehearsal	awaiting decision
—	Rollback procedure	dry-run pending
○	Final payment service live	this week
○	Executive go / no-go	25 Jun

Decision today: run a full peak-load rehearsal before cutover.

RUN THE PEAK-LOAD REHEARSAL

One day of effort buys certainty that checkout holds at Black-Friday volume.

CUT OVER ON SYNTHETIC TESTS ONLY

Saves a day but leaves the highest-impact risk unrehearsed on launch day.

PRIYA VENKAT · PLATFORM-TEAM@LUMEN.EXAMPLE

On track for 1 July —
pending your call on
load testing.
